



Feature, Not a Bug

Sprint #1 Review

ALEX HANUS

JARRET FOSSEN

JOSE ORDONEZ

AMARI THOMAS

OSBALDO OROZCO

The ReadyPets Vision

For pet owners and trusted caregivers who need a reliable way to protect pets during an emergency, ReadyPets is a secure digital emergency-planning platform that keeps rescue information, care instructions, and caregiver plans in one place. Unlike static “Pets Inside” stickers or informal paper and text-message plans, ReadyPets keeps critical information current, protects it from unauthorized access, and makes it reliably available to authorized caregivers and emergency responders when it matters most.

Sprint 1 Goal

Main goal:

Establish the product and technical foundation needed to begin implementation.

- ▶ Configure the repository and core frameworks
- ▶ Clarify the product scope by reviewing the sponsor prototype and client requirements
- ▶ Create an initial Jira backlog with work items the team can estimate

Sprint #1 Backlog

Outcome	Completed Work	Estimate	Actual effort
Development foundation	Repository, project structure, dependencies, and documentation	Not recorded	4 hrs
Product understanding	Ran, documented, and mapped the sponsor prototype	Not recorded	20+ hrs
Technical direction	Selected the initial technology stack	Not recorded	5 hrs


Prototype Analysis and Documentation

Work completed

- Ran the sponsor's prototype locally
- Captured and numbered accessible pages
- Documented navigation and purpose of each page

How this helps

- Gives the team a shared reference for development
- Helps turn the prototype into clearer requirements and backlog items
- Provides a baseline for future discussions with sponsor

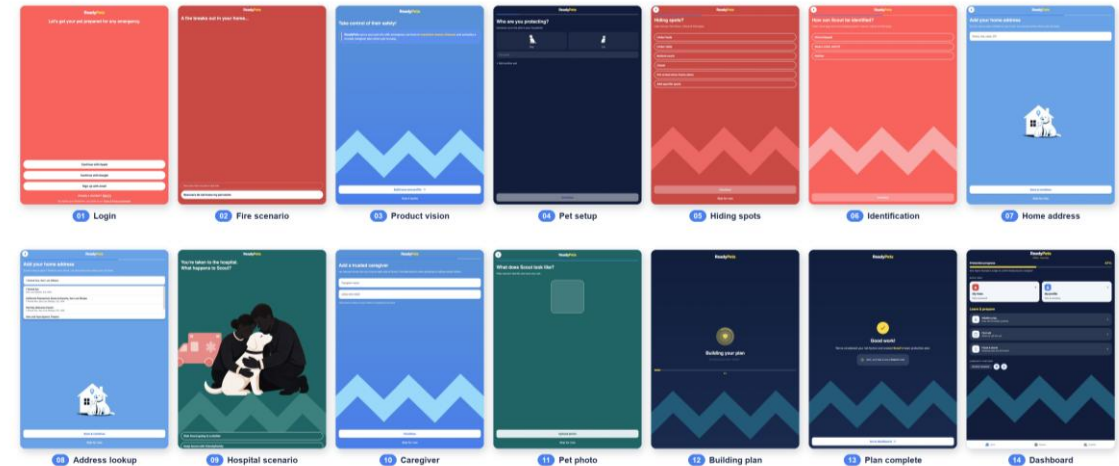

Onboarding

No.	Screen	File	How reached	Notes
001	Login	001-login.png	Initial application screen	Authentication choices are visual placeholders; every option enters the same local flow.
002	Fire scenario	002-fire-scenario.png	Sign up with email	Frames the problem through an emergency scenario. The hero image remained visually transparent in the web build during capture.
003	Product introduction	003-product-introduction.png	Choose "Rescuers do not know my pet exists"	States the core promise: synchronize pet information, improve rescue chances, and activate caregivers.
004	Household pets	004-household-pets.png	Build your pet profile	Collects pet type and name; supports adding multiple pets. Test pet: Scout, dog.
005	Hiding spots	005-hiding-spots.png	Continue after defining the household pet	Collects likely rescue locations and crate status. "Under beds" selected for the walkthrough.
006	Identification	006-identification.png	Continue from hiding spots	Collects microchip and collar-ID status.
007	Home address	007-home-address.png	Continue from identification	Connects the rescue plan to a household location.

Design/Tech Decisions

Cross-platform applications

- ▶ React Native and Expo let us build one mobile application for iOS and Android.
- ▶ React and TypeScript give the web and mobile teams familiar tools.

One shared backend

- ▶ A NestJS API serves both applications and contains the business rules.
- ▶ PostgreSQL supports the relationships among households, pets, owners, caregivers, and permissions.

Security controlled by the backend

- ▶ Supabase provides Google and Apple authentication during development.
- ▶ NestJS verifies each user and controls which ReadyPets data they can access.
- ▶ Database credentials remain on the backend.

Team development

- ▶ A TypeScript monorepo provides shared API contracts and consistent tooling.
- ▶ GitHub Actions will check code quality, tests, and builds.

Metrics

Results

- ▶ 6 completed work items recorded in Jira
- ▶ Sponsor prototype reviewed and documented
- ▶ Repository, project structure and technology stack established
- ▶ Communication channels establish for the team and sponsor
- ▶ The time required for meetings, scheduling, access requests, and sponsor communication was difficult to estimate in advance
- ▶ Because this coordination work was not estimated at the start of Sprint 1, meaningful burndown and velocity metrics are not available

Sprint 2 measurement plan

- ▶ 40 person-hours estimated before the sprint begins
- ▶ Remaining estimated hours tracked throughout the sprint for the burndown chart
- ▶ Estimated hours of completed work used as our first velocity baseline
- ▶ Actual hours compared with estimates for each backlog item

Sprint 1 Retrospective

What went well

- ▶ We developed a clearer understanding of the sponsor's vision and prototype.
- ▶ Established the repository, project structure, and technology stack
- ▶ Created dedicated channels for team coordination, client communication, and urgent messages.
- ▶ Built an initial backlog that gives us a clear starting point for development

What we will improve

- ▶ Estimate, prioritize, and assign Jira tasks before each sprint begins
- ▶ Raise blockers and concerns as soon as they arise
- ▶ Continue independent work while waiting for sponsor input or access
- ▶ Plan a demonstrable product feature for the next sprint

Sprint 2 Tentative Plan

Sprint 2 Goal:

Build a working pet-profile system that allows someone to create a profile, save it, and return later to view it.

Sprint backlog item	Estimated effort
Create the initial mobile app and backend	8 hrs
Design the database schema and connect PostgreSQL	7 hrs
Build and test the APIs for saving and retrieving pet profiles	8 hrs
Build the mobile app interface for creating and viewing pet profiles	10 hrs
Connect the mobile app to the backend and verify that profiles can be saved and loaded	7 hrs
Total planned effort	40 hrs
