
Sprint #2

The Recruiters

Babaldeep Thiara
Yaneli Cruz
Morgan Blanck
Amelia Harris

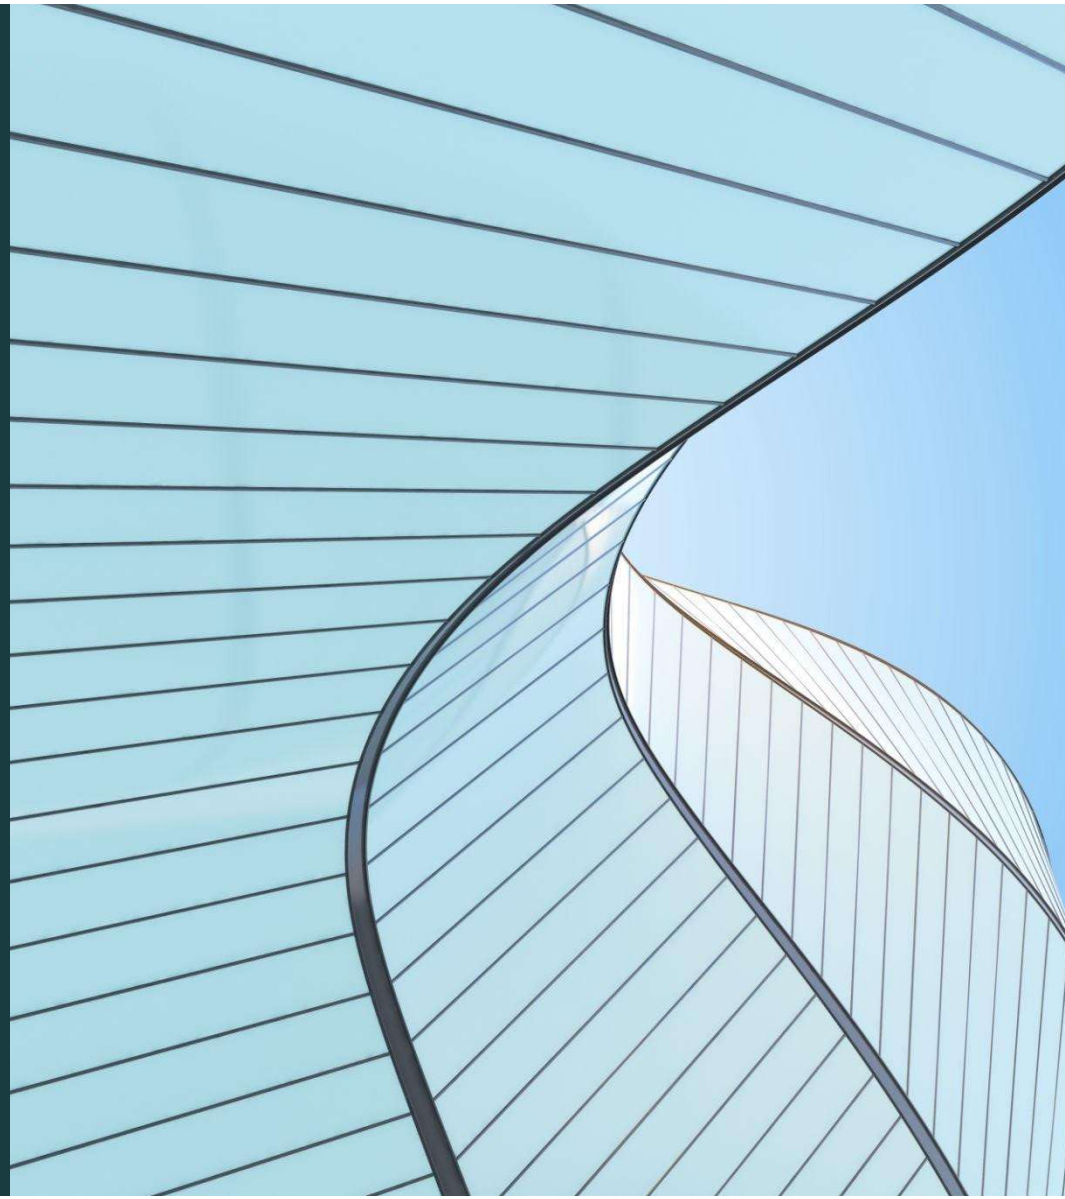

Sprint 2 Goals

- ★ Main Goal: Design
- ★ Continued developing the frontend
- ★ Database design
- ★ More outreach to Cal Poly resources
- ★ Updating documentation
- ★ AI Chatbot research




Sprint #2 Backlog

Backlog (10 work items) 61 0 0 Create sprint


TR-17 Sign up Page		To Do	8
TR-16 Login Page		To Do	8
TR-18 Job Page		To Do	8
TR-22 Chatbot Box		To Do	8
TR-23 Chatbot		To Do	8
TR-31 Event/Job Post Component		To Do	4
TR-32 Profile Page		To Do	8
TR-69 Sign in/Sign Up Logic		To Do	4
TR-70 User Data Design		To Do	2
TR-71 Tech Spec		To Do	3

+ Create

UI Prototype

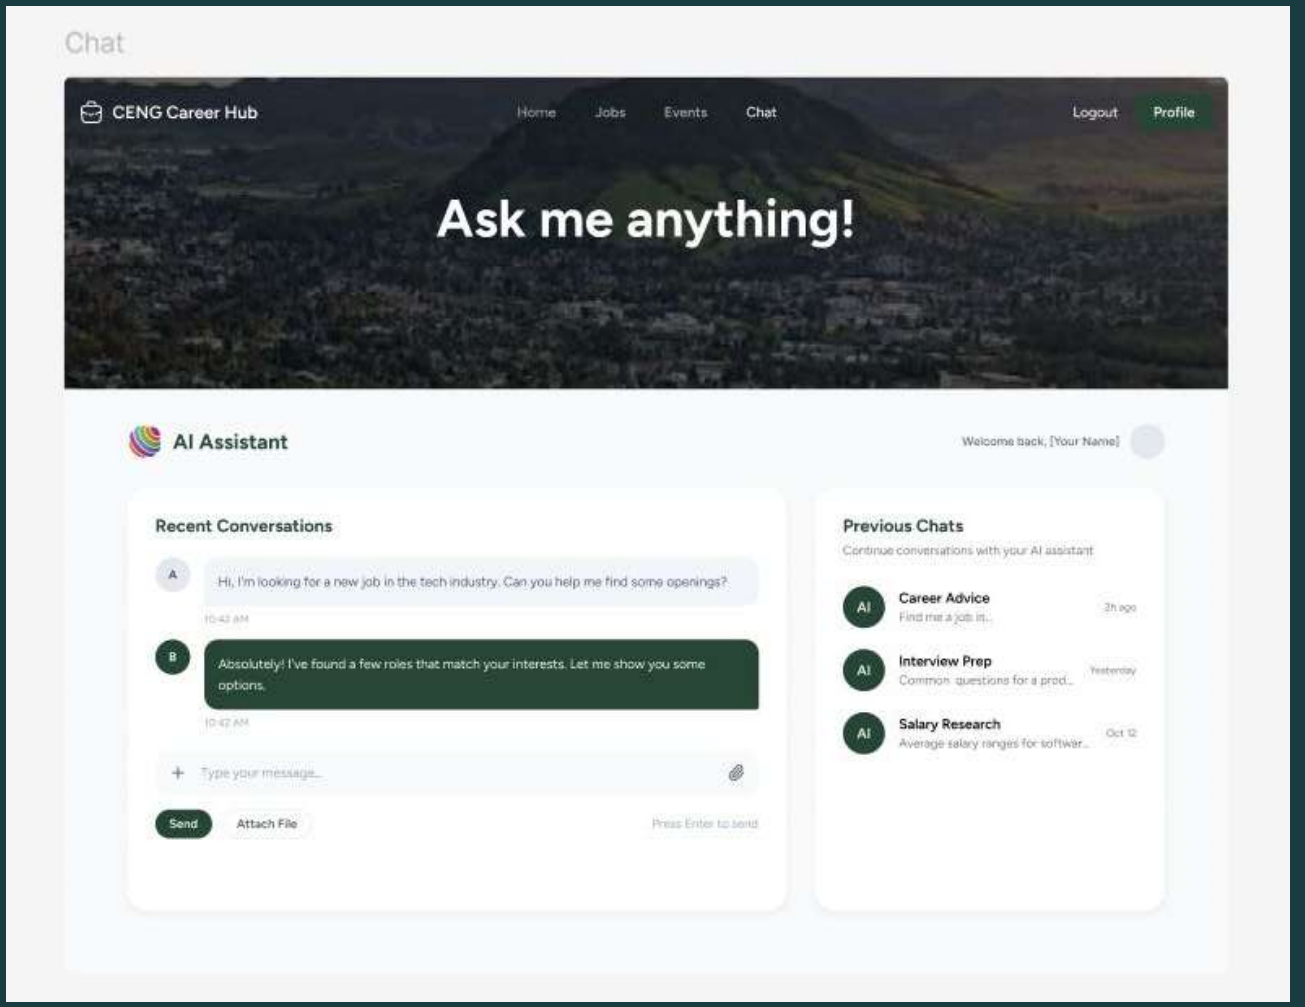

Design Diagram

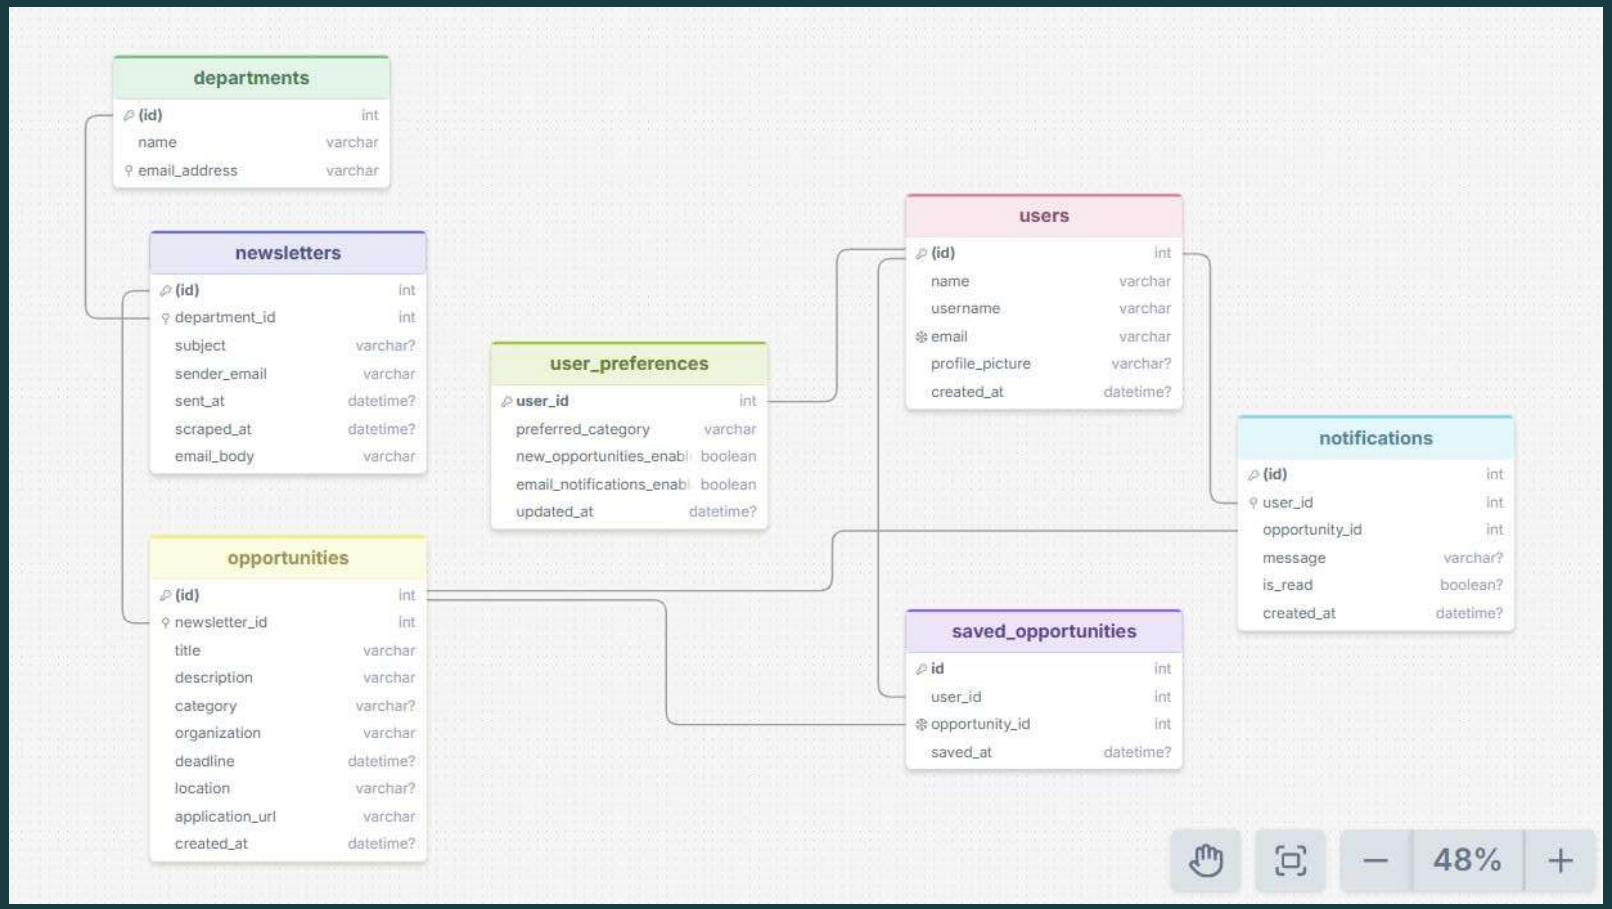

Design and Tech decisions made or considering

LlamaIndex for AI Chatbot


- ★ pros: known for not hallucinating, cheaper than other models
- ★ cons: may be more difficult to connect with PostgreSQL

Libraries for Integration

- ★ LangChain: uses a react agent to query model which helps prevent hallucinations
- ★ Pydantic AI: Python library that helps build agents

Demo

Metric

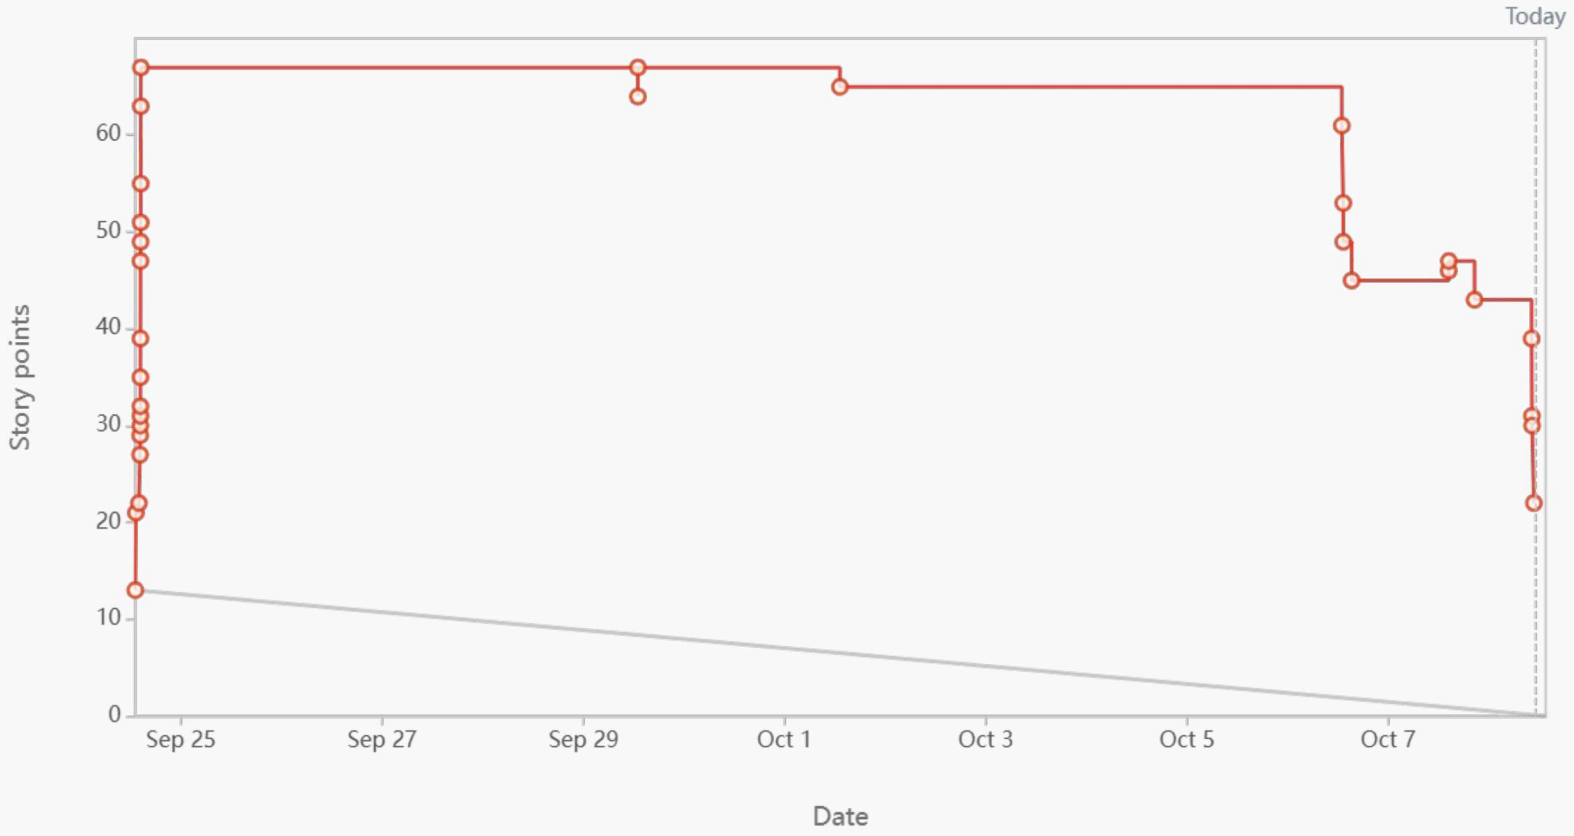
Today
Story points
60
50
40
30
20
10
0
Sep 25
Sep 27
Sep 29
Oct 1
Oct 3
Oct 5
Oct 7
Date

Retrospective

What went well:

- ★ started pair programming
- ★ making progress on outreach and being added to newsletters
- ★ designed database

What didn't go well:

- ★ based on burndown chart, we completed most of our tasks near the end of the Sprint
- ★ overestimated the number of tasks we would be able to complete
- ★ current way of making tasks with subtasks doesn't work with jira well

How we will improve:

- ★ spread out our tasks throughout the Sprint
- ★ better Sprint planning and distribution of tasks
- ★ assigning subtasks to tasks differently

Planning

- ★ Making the database (not yet implemented to frontend... #sprint4)!
  - Adding all data to it... might be ambitious but we'll try to get it done
- ★ Work on technical specifications document
- ★ Continue creating frontend components and developing main pages

Thank you!
